AUDIT_2026-03-10_202500

AutoAllies Iteration Productivity Audit — Iteration 6.5

Audit Date: 2026-03-10T20:25:00Z (Updated with GitHub data)
Auditor: Ramon Aseniero Jr. — Engineering Productivity Engineer
Framework: SAFe (Scaled Agile Framework)
Report Type: Iteration-Bounded Productivity Audit (Full)

Audit Boundary

Parameter	Value
ADO Organization	`jairo`
ADO Project	`Auto Allies` (ID: `2d7af571-6ef6-4ad0-a509-c440e008b0fb`)
ADO Team	`AA Development Team` (Board ID: `330e6bf1-3515-443c-a2d8-b84f46c38f57`)
Board / Backlog	`Stories and Deliverables`
Current Iteration	**Iteration 6.5**
Iteration Start	2026-03-09
Iteration Finish	2026-03-22
Iteration Day at Audit	Day 2 of 14 (14% elapsed)
GitHub Repo — Frontend	`jairosoft-com/autoallies-version2` (TypeScript / Next.js)
GitHub Repo — Backend	`jairosoft-com/autoallies-api-core` (PHP / Laravel)

> **Scope Note:** No other ADO boards, teams, projects, or GitHub repositories were analyzed. This audit is strictly bounded to the above sources.

Data Availability

Source	Status
ADO Iteration Settings	✅ Available
ADO Work Items (Iteration 6.5)	✅ Available
ADO Team Capacity	✅ Available
GitHub — `autoallies-version2`	✅ Available
GitHub — `autoallies-api-core`	✅ Available

---

1. Executive Summary

Iteration 6.5 began on March 9, 2026, and this audit runs on Day 2 of a 14-day sprint. The team has **12 parent work items** (5 User Stories, 3 Enablers, 2 Spikes, 1 Defect) containing **62 child tasks** across 5 team members.

ADO progress is minimal: only **4 tasks are closed** (6.5%), **3 are active** (4.8%), and **55 remain in New state** (88.7%). However, GitHub tells a different story — **10 commits** were pushed and **1 PR merged** on March 9 alone. The critical disconnect is that **zero GitHub artifacts reference any ADO work item ID**, making cross-system traceability non-existent.

Critical Findings:

#	Finding	Severity	Source
1	**Zero ADO-GitHub traceability** — no work item IDs in any branch, commit, or PR	🔴 CRITICAL	Cross-system

#	Finding	Severity	Source
2	**Zero code reviews** — PR #65 self-merged with 0 reviewers; Earl pushes direct to develop/dev bypassing PRs entirely	🔴 CRITICAL	GitHub
3	**Zero branch protection** — all 57 branches across both repos are unprotected	🔴 CRITICAL	GitHub
4	**Ownership imbalance** — Earl owns 42% of ADO tasks AND is the only active committer in both repos	🔴 HIGH	Cross-system
5	**Cliff has zero GitHub activity** despite owning 12 iteration tasks	🟡 MEDIUM	Cross-system
6	**Poor commit hygiene** — 50% of iteration commits are labeled `_clean` with no meaningful description	🟡 MEDIUM	GitHub
7	**Production defect #200773** sitting in New state with no investigation	🟡 MEDIUM	ADO

Weighted Team Health Score: 25/100 — Critical state requiring immediate process intervention.

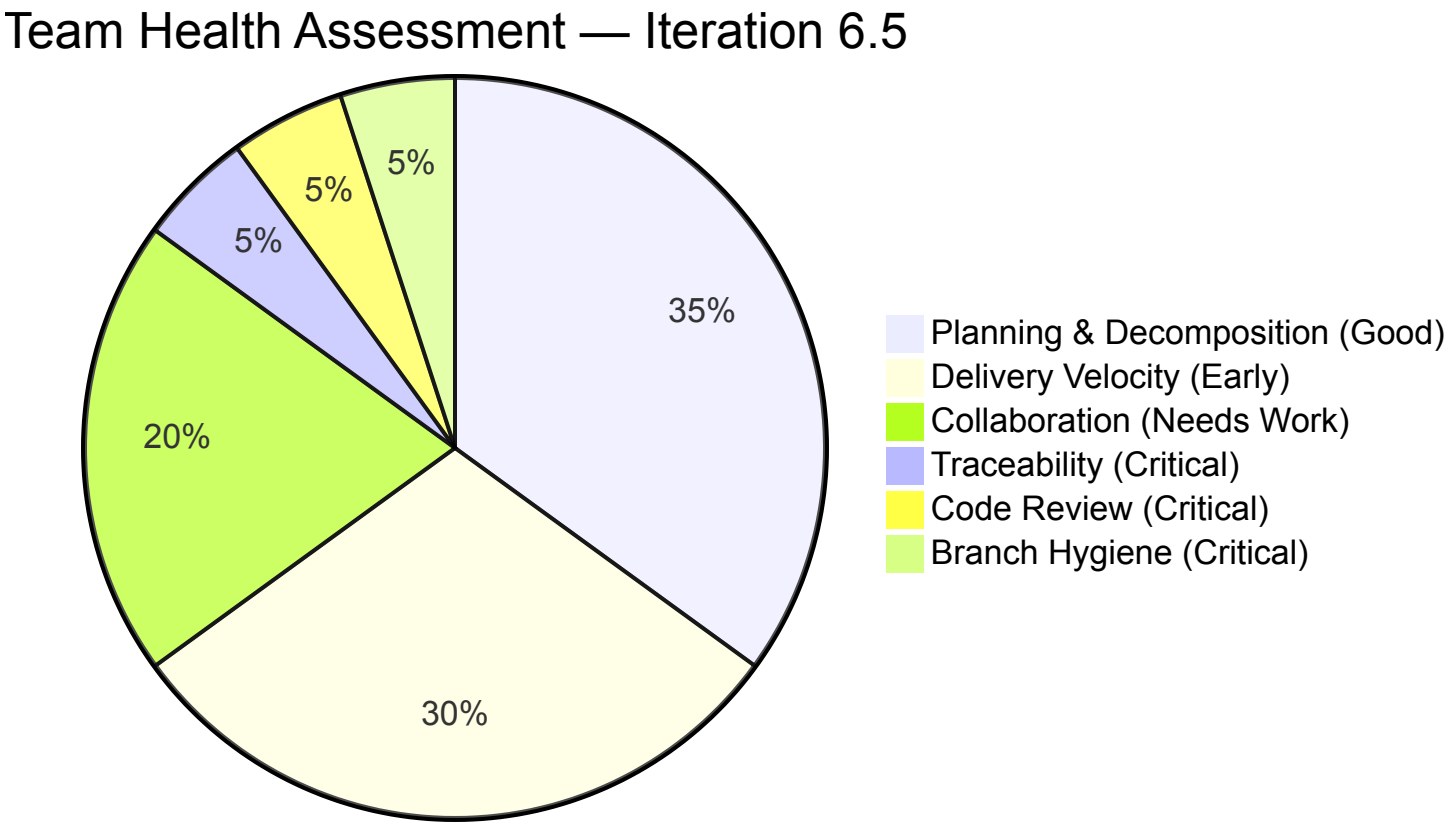

---

2. Iteration Scope & Methodology

2.1 Planned Work Items

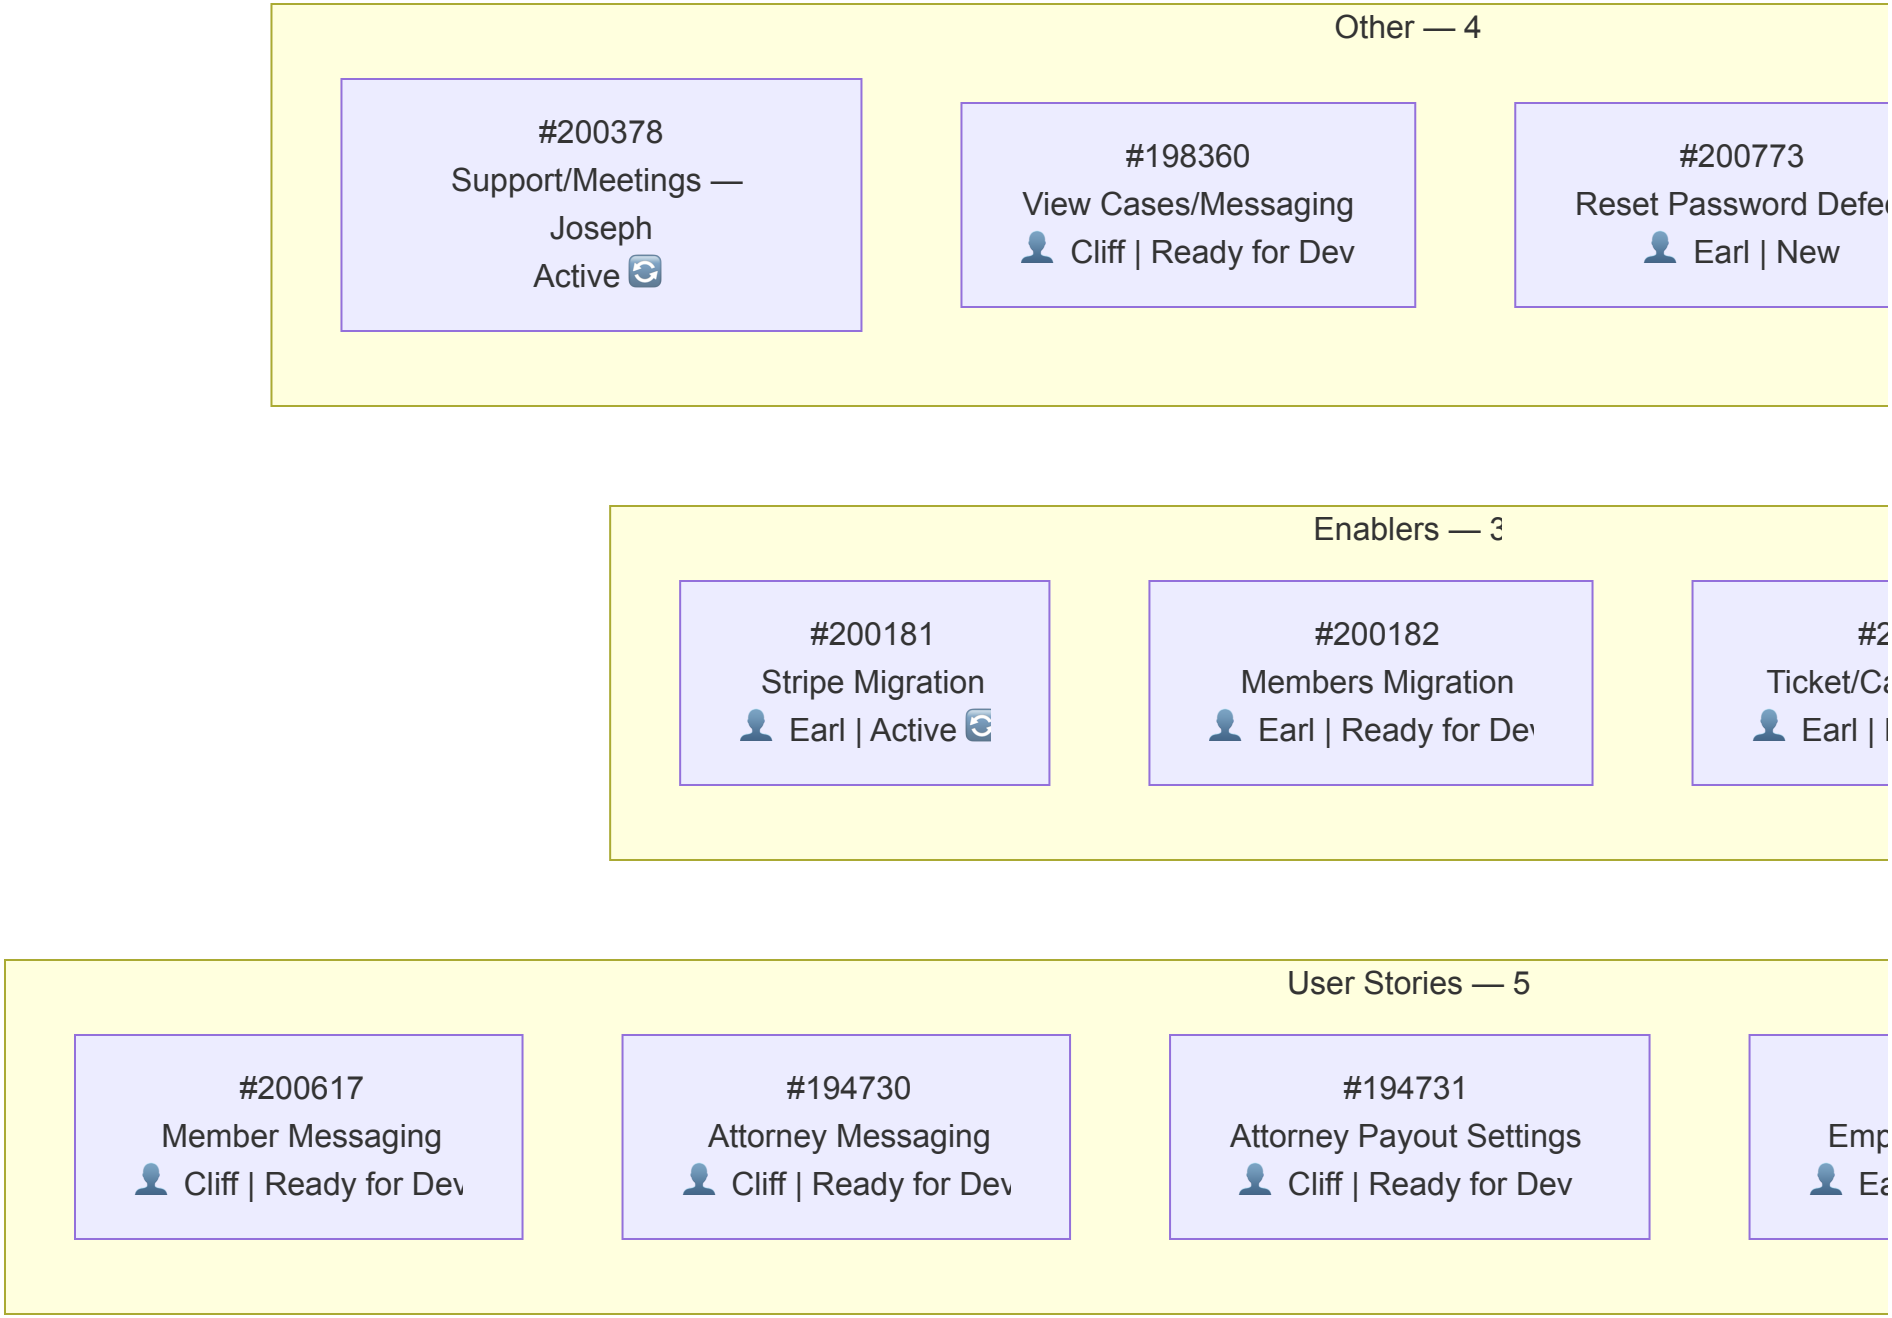

2.2 Work Item State Distribution

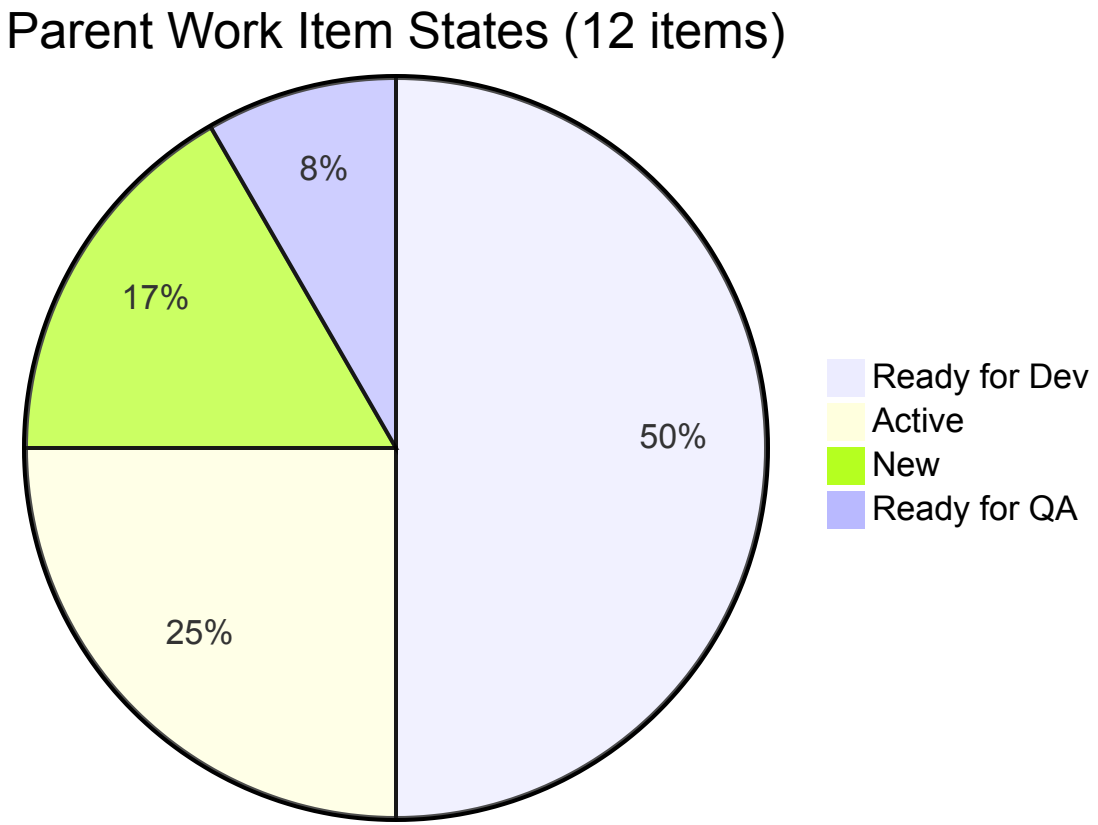

2.3 Task State Distribution

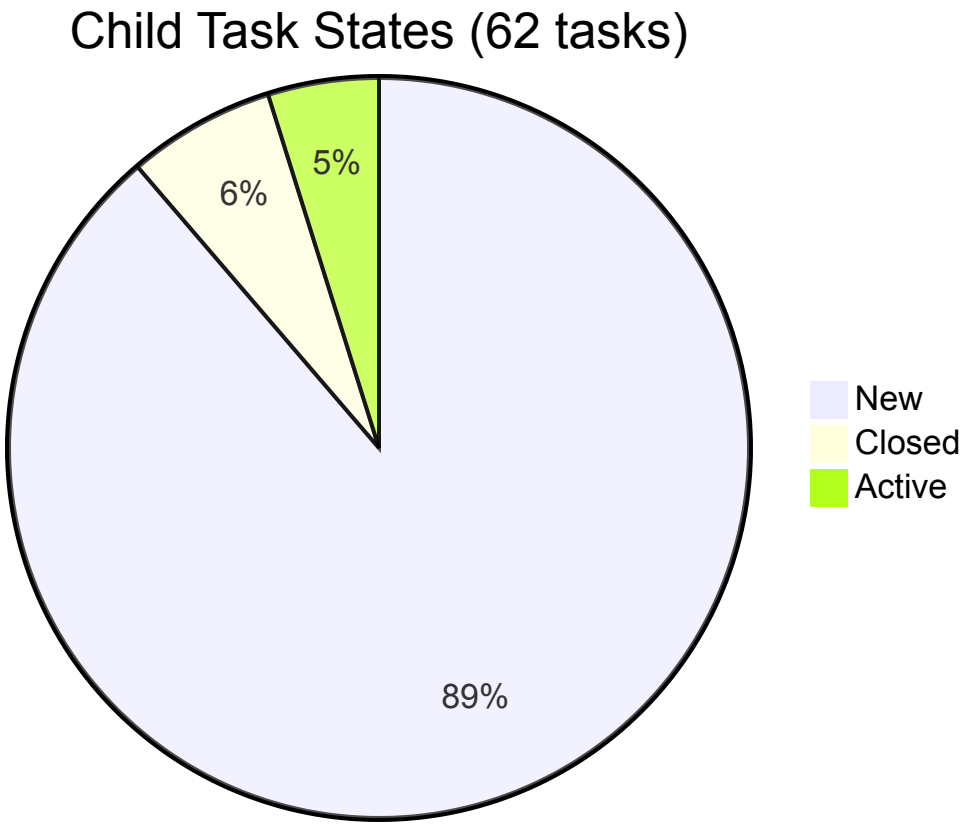

---

3. Developer Productivity Findings

3.1 Team Capacity Overview

Developer	Activity	Cap/Day	Days Off	ADO Tasks	Closed	Active	New	GitHub Commits (Iter)	GitHub PRs (Iter)
Earl Carino	Dev	6h	Mar 20	26	3	1	22	7	0 (direct push)

Developer	Activity	Cap/Day	Days Off	ADO Tasks	Closed	Active	New	GitHub Commits (Iter)	GitHub PRs (Iter)
Joseph Gerona	Dev	4h	—	18	1	2	15	3	1 (merged, self)
Cliff Carcueva	Dev	6h	Mar 20	12	0	0	12	0	0
Jerlyn Ates	Req+Test	6h	—	6	0	0	6	0	0
Roden Cole	Deploy	2h	—	0	0	0	0	0	0
TOTAL	—	**24h**	**2**	**62**	**4**	**3**	**55**	**10**	**1**

3.2 Task Ownership vs. GitHub Activity

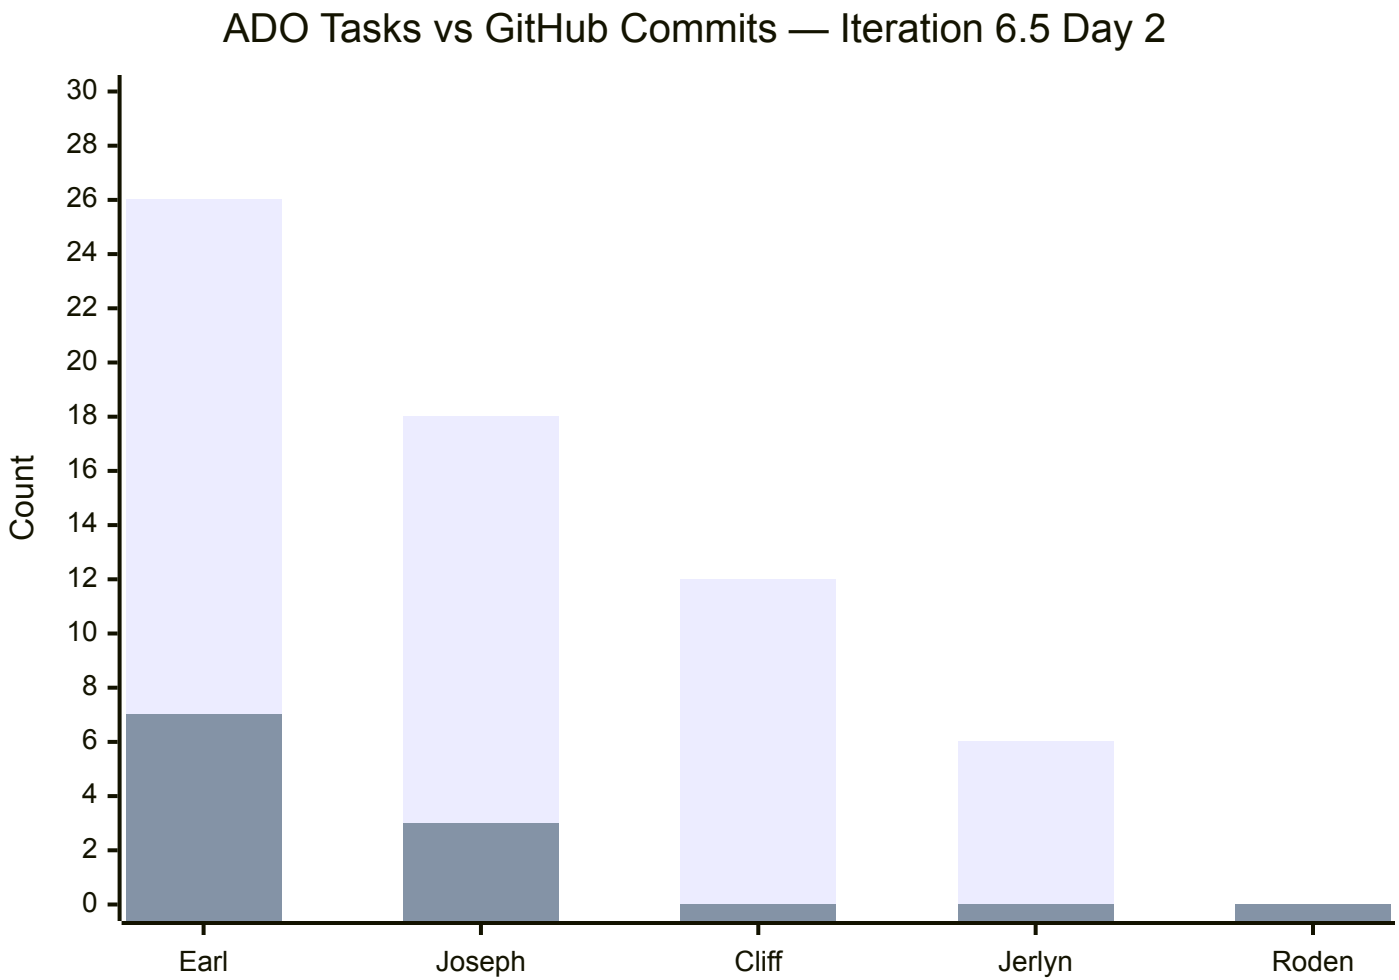

3.3 Individual Developer Analysis

Earl Carino (ecarinoJS) — Highest Output, Bypasses PR Workflow

Earl owns **42% of all iteration tasks** (26/62) and is the **most active committer**, with 7 commits across both repos on Day 1 alone. However, every one of those commits was pushed **directly to develop/dev without a PR**. He is bypassing the pull request workflow entirely.

Metric	Value
ADO tasks owned	26 (42% of total)
ADO tasks closed	3 (#200441, #200444, #200445 — Employee Login)
GitHub commits in iteration	5 on frontend develop, 2 on backend dev
GitHub PRs in iteration	**0** — all direct pushes
Code review participation	**0** reviews given or received
Commit message quality	Poor — 3 of 5 frontend commits labeled `_clean`
ADO work item IDs in commits	**0** — zero traceability

Commit detail (March 9, iteration window):

Time (UTC)	Repo	Message	Traceability
01:28	Frontend	`add ticket post log`	❌ No WI ID
01:32	Frontend	`Merge branch 'develop'...`	❌ Merge noise
02:01	Backend	`Ticket submission post log`	❌ No WI ID
02:21	Backend	`get active status of a member`	❌ No WI ID
02:42	Frontend	`_clean`	❌ No WI ID
09:13	Frontend	`_clean`	❌ No WI ID
09:16	Frontend	`_clean`	❌ No WI ID

Assessment: Earl is delivering real work (Employee Login story moved to Ready for QA, Stripe migration active) but his workflow completely bypasses quality gates. Direct pushes to integration branches with no reviews and no traceability is the single biggest process risk on this team.

Source: ADO + GitHub

Joseph Gerona (JosephJairo) — Feature Delivery with Self-Merge

Joseph created and merged **PR #65** ("Feature/member attorney cases") into develop on March 9. The PR was **self-merged with 0 reviews** — he opened it at 01:06 and merged at 01:26, a **20-minute cycle time**. He also made 3 commits on his feature branch for the Members and Attorneys lists feature.

Metric	Value
ADO tasks owned	18 (10 meetings + 8 feature)
ADO tasks closed	1 (#200379 — Meeting March 9)
GitHub commits in iteration	3 (feature work + config revert)
GitHub PRs in iteration	1 (PR #65 — merged, self-merged)
PR cycle time	20 minutes (open → merge)
Code reviews given	**0**
Code reviews received	**0**
ADO work item IDs in commits/PR	**0** — zero traceability

Assessment: Joseph is the only developer using the PR workflow, which is positive. However, self-merging with zero reviews negates the value of PRs as a quality gate. His meeting/support spike (#200378) consumes 56% of his tracked tasks, leaving limited capacity for the Case List feature (#198359).

Source: ADO + GitHub

Cliff Carcueva (ccarcuevajairo) — Zero Iteration Activity

Cliff owns 4 user stories (#200617, #194730, #194731, #198360) with **12 tasks — all in New state**. He has **zero commits and zero PRs** in the iteration window. His last GitHub activity was PR #62 (frontend) on February 27, which is outside this iteration.

Metric	Value
ADO tasks owned	12 (across 4 stories)
ADO tasks closed	0
GitHub commits in iteration	**0**
GitHub PRs in iteration	**0**
Last GitHub activity	Feb 27 (PR #62, bug/ticket-upload-clif)

Assessment: Day 2 of a 14-day sprint with zero activity is an early warning signal. Cliff has 4 features to deliver requiring both frontend and backend work. Without immediate task activation, he faces a compression risk in the second half of the iteration.

Source: ADO + GitHub

Jerlyn Ates — QA Gated on Development Completion

Jerlyn has 6 QA testing tasks, all in **New** state. This is expected — she cannot test until developers deliver. Only story #194650 (Employee Login) has reached "Ready for QA," which should unblock her first task.

Source: ADO

Roden Cole — No Tasks, No Visibility

Roden has deployment capacity (2h/day) but **zero tasks in the iteration** and **zero GitHub activity**. His work, if any, is completely invisible to the audit.

Source: ADO + GitHub

---

4. ADO-to-GitHub Traceability Analysis

4.1 Traceability Audit

This is the most critical finding of this audit. **Zero GitHub artifacts in the iteration window reference any ADO work item ID.**

GitHub Artifact	ADO Work Item Reference	Status
PR #65 title: "Feature/member attorney cases"	No WI ID	❌
PR #65 body: "Merge to develop changes made for Members and Attorneys Lists Feature"	No WI ID	❌
Branch: `feature/member-attorney-cases`	No WI ID	❌
Commit: "commit for all changes done for Members and Attorneys lists"	No WI ID	❌
Commit: "revert changes for config"	No WI ID	❌
Commit: "add ticket post log"	No WI ID	❌
Commit: "Ticket submission post log"	No WI ID	❌
Commit: "get active status of a member"	No WI ID	❌
Commit: "_clean" (×3)	No WI ID	❌

4.2 Work Classification

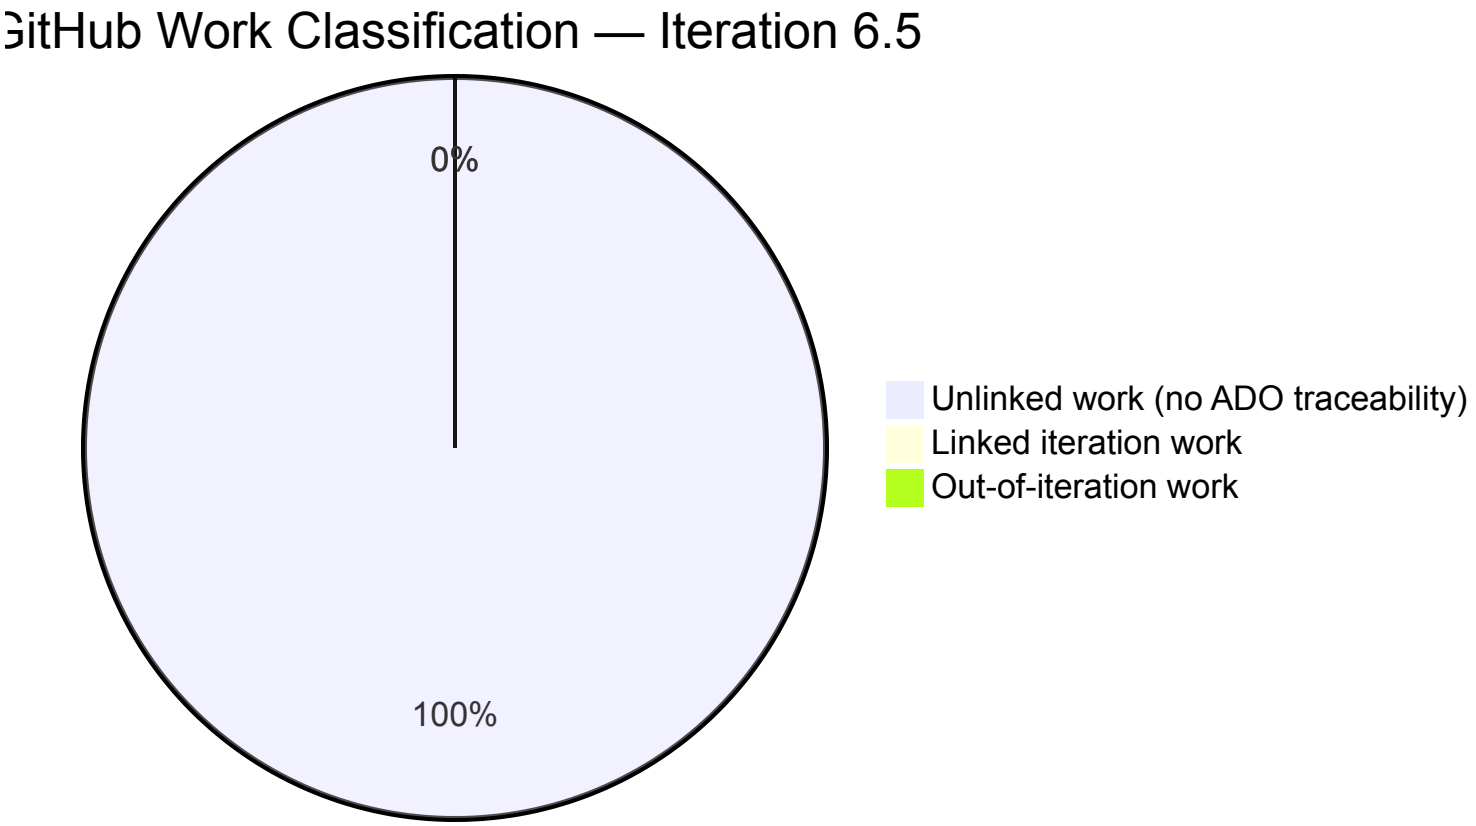

Classification	Count	Details
Linked iteration work	0	No GitHub artifact references an ADO work item ID
Unlinked work	10 commits, 1 PR	All iteration GitHub activity lacks ADO traceability
Out-of-iteration work	0	No commits from outside iteration dates on Day 2
Maintenance/context only	3 commits	`_clean` commits by Earl (no functional description)

4.3 Inferred Correlation (Best-Effort)

While no formal links exist, we can attempt semantic matching between ADO stories and GitHub activity:

ADO Item	Likely GitHub Activity	Confidence
#194650 (Employee Login) — Ready for QA	Earl's direct commits (ticket post log, active status)	🟡 Low
#198359 (Case List) — Active	Joseph's PR #65 (member-attorney-cases)	🟡 Low
#200181 (Stripe Migration) — Active	No matching commits found	❌ None
Cliff's 4 stories	No GitHub activity	❌ None

> **Auditor Note:** Semantic correlation is unreliable without formal ID references. The team must adopt a traceability convention (e.g., `AB#200617` in commit messages, branch naming like `story/200617-member-messaging`) to enable verifiable audit trails.

---

5. PR Throughput, Cycle Time & Merge Behavior

5.1 Iteration PR Summary

Metric	Frontend	Backend	Combined
PRs created in iteration	1	0	1
PRs merged in iteration	1	0	1
PRs with reviews	0	0	**0**
Self-merged PRs	1 (100%)	—	**100%**
Average cycle time	20 min	—	20 min
Direct pushes to integration branch	5 commits	2 commits	**7 commits**

5.2 Historical PR Pattern (Context)

Looking at the full PR history to assess systemic patterns:

Metric	Frontend (65 PRs)	Backend (25 PRs)
Total PRs ever	65	25
PRs with any review	**0**	**0**
Self-merge rate	~85%	~92%
Empty PR body rate	~69%	~80%
Avg time open→merge	< 1 minute (most)	< 1 minute (most)

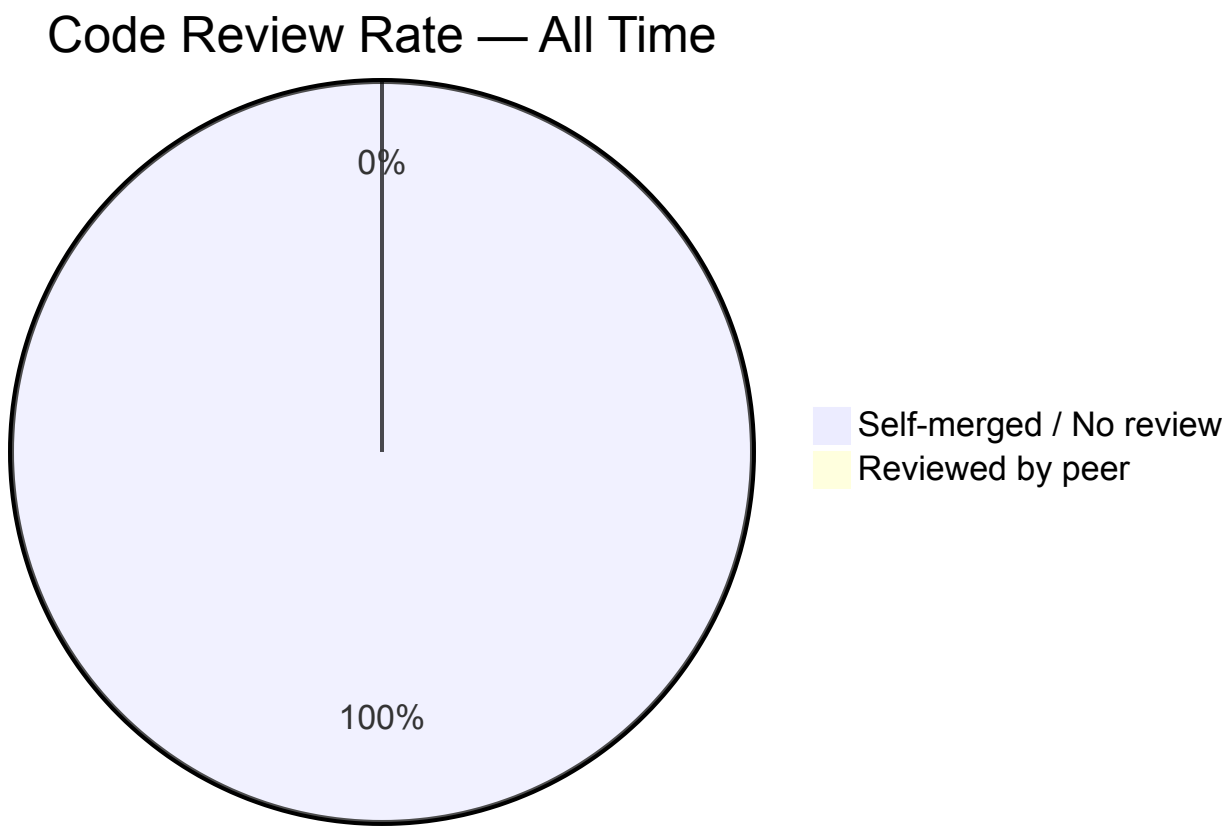

> **Critical:** Across 90 total PRs in the project's lifetime, **zero have ever received a code review**. This represents a complete absence of the code review practice.

5.3 Direct Push Analysis

Earl pushed 7 commits directly to integration branches (develop/dev) without PRs on March 9 — Day 1 of the iteration. This means the majority of code changes in this iteration bypassed the PR workflow entirely.

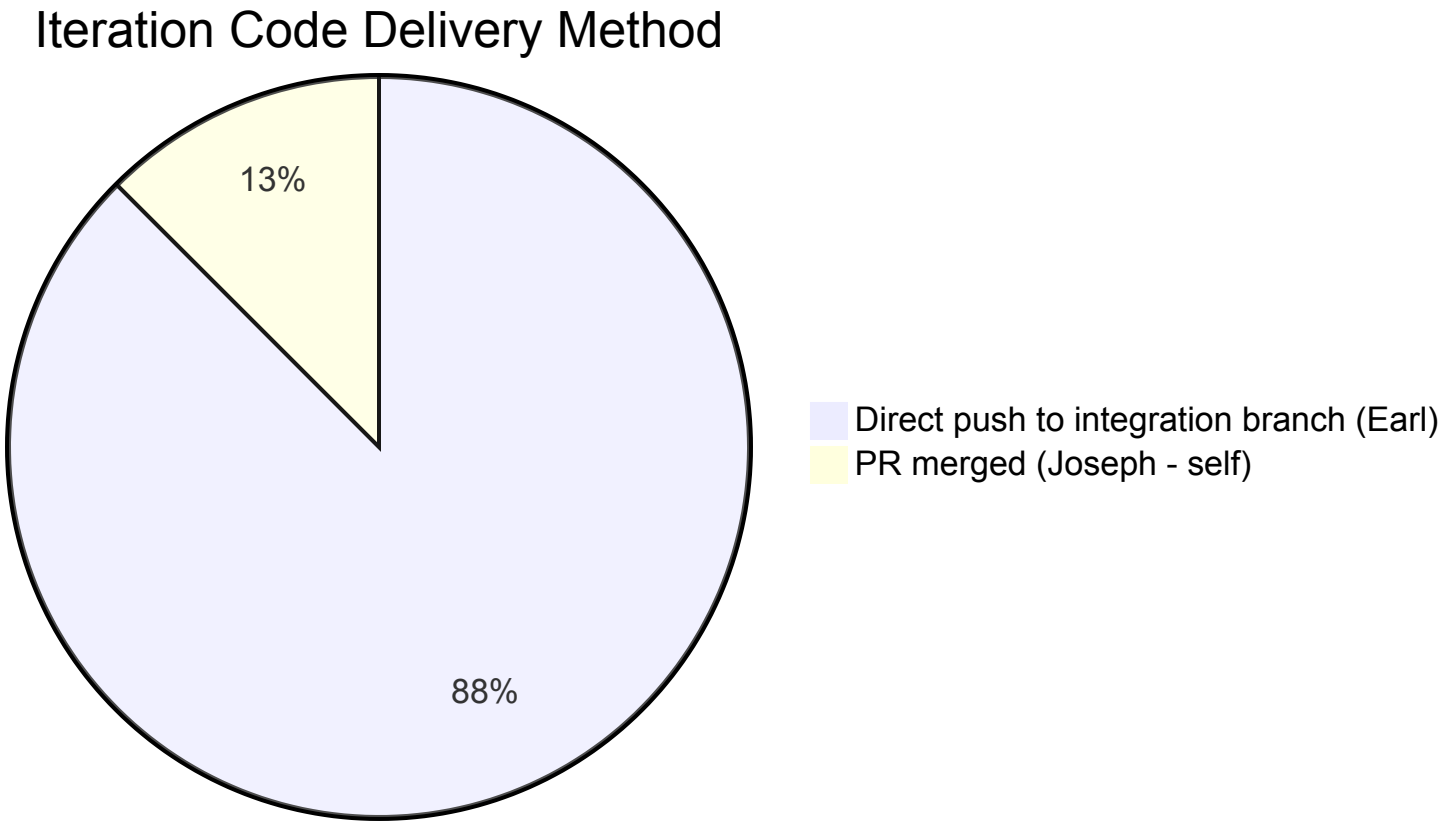

---

6. Collaboration & Review Analysis

6.1 Review Participation Matrix

Reviewer ↓ / Author →	Earl	Joseph	Cliff	Jerlyn	Roden
Earl	—	❌	❌	—	—
Joseph	❌	—	❌	—	—
Cliff	❌	❌	—	—	—
Jerlyn	—	—	—	—	—
Roden	—	—	—	—	—

> ❌ = No reviews exchanged. The matrix is entirely empty — no developer has ever reviewed another developer's code in these repositories.

6.2 Collaboration Signals

Signal	Status	Evidence
Cross-developer code review	❌ None	0 reviews across 90 lifetime PRs
Pair programming indicators	❌ None	No co-authored commits
Cross-repo collaboration	⚠️ Minimal	Earl works in both repos; others are single-repo
QA-Dev handoff	⚠️ Delayed	Only 1 of 12 parent items has reached QA
Deployment coordination	❌ Invisible	Roden has no tasks or commits

6.3 Work Dependency Map

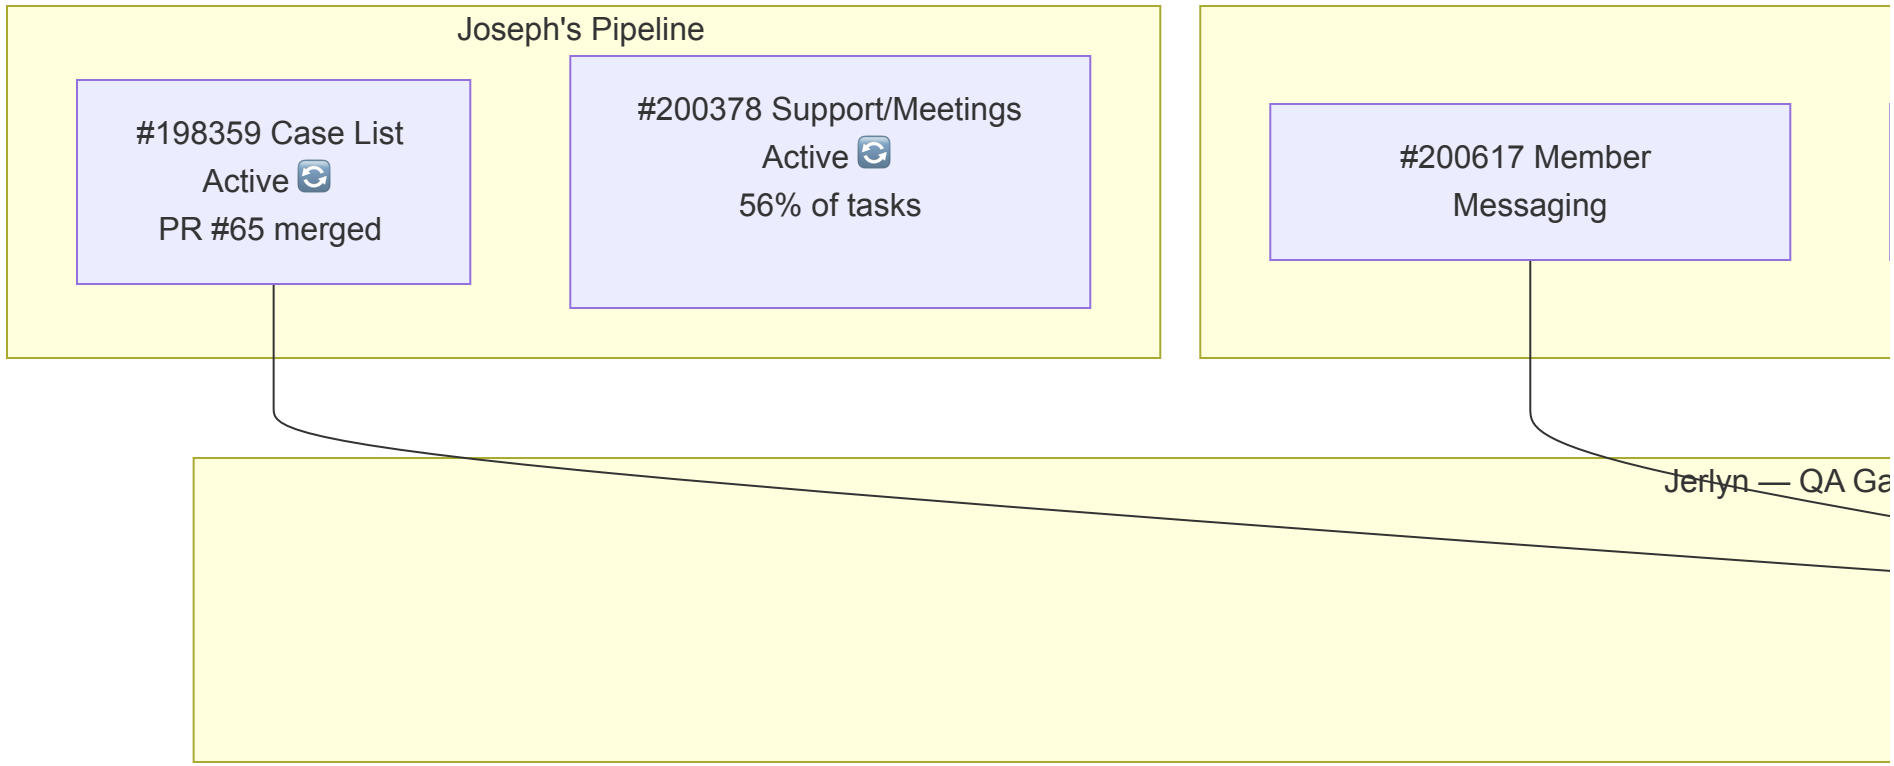

---

7. Repo Hygiene & Productivity Enablers

7.1 Branch Protection

Repo	Protected Branches	Status
Frontend (`autoallies-version2`)	0 of 41	🔴 CRITICAL
Backend (`autoallies-api-core`)	0 of 16	🔴 CRITICAL

> **Impact:** Without branch protection, any developer can push directly to `develop` , `dev` , `main` , or `staging` without review. Earl is actively exploiting this gap by pushing directly to integration branches.

7.2 Repo Configuration

Check	Frontend	Backend
Branch protection on develop/dev	❌	❌
Branch protection on main	❌	❌
CODEOWNERS file	❌	❌
PR template	❌	❌
CI/CD quality gates (lint, test)	❌	❌
GitHub Actions workflows	✅ (deploy only)	✅ (deploy only)
Conventional commits	❌ (~3% adoption)	❌ (~2% adoption)
Consistent branch naming	⚠️ Mixed	⚠️ Mixed
Dev branch naming	`develop`	`dev` (inconsistent)

7.3 Branch Hygiene

Metric	Frontend	Backend	Total
Total branches	41	16	**57**
Protected branches	0	0	**0**

Metric	Frontend	Backend	Total
Stale branches (merged, not deleted)	~30+	~10+	**~40+**

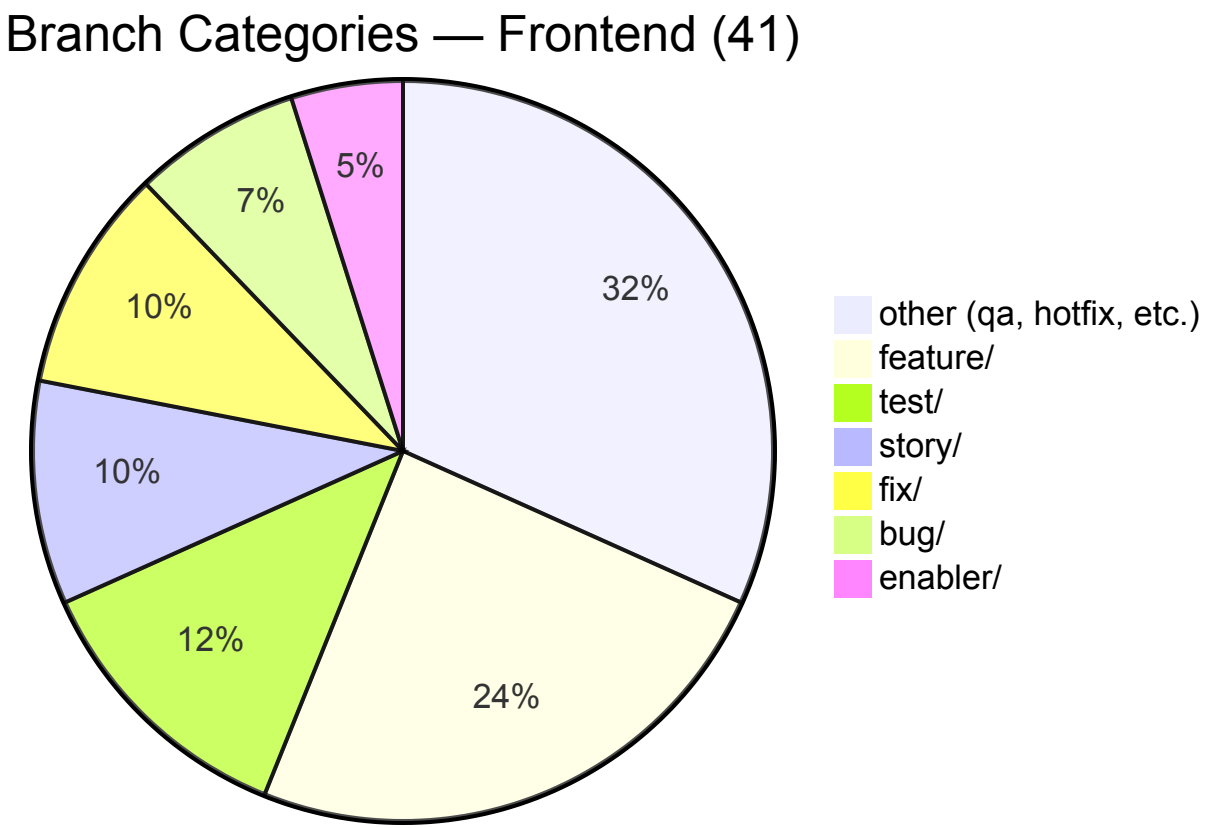

> 5+ different branch prefix conventions are in use with no standardization.

---

8. Risks & Bottlenecks

8.1 Risk Matrix

#	Risk	Severity	Source	Affected
R1	**Zero code reviews — ever**	🔴 CRITICAL	GitHub	Code quality, knowledge sharing, bus factor
R2	**Zero ADO-GitHub traceability**	🔴 CRITICAL	Cross-system	Audit capability, compliance, delivery verification
R3	**Zero branch protection** on any branch	🔴 CRITICAL	GitHub	Code integrity, rollback safety
R4	**Earl single-point-of-failure** — 42% of tasks + only active multi-repo committer + direct pushes	🔴 HIGH	Cross-system	Entire team delivery
R5	**Cliff zero activity** on Day 2 with 12 tasks across 4 stories	🟡 MEDIUM	Cross-system	4 user stories
R6	**Production defect #200773** in New state	🟡 MEDIUM	ADO	End-user impact
R7	**QA bottleneck** — all 6 QA tasks blocked on dev completion	🟡 MEDIUM	ADO	Sprint completion
R8	**Joseph meeting overhead** — 56% of tasks are meetings	🟡 MEDIUM	ADO	Case List feature
R9	**Roden has zero tasks + zero activity**	🟡 MEDIUM	Cross-system	Deployment visibility
R10	**Unassigned spike #200780** (Network DNS)	🟢 LOW	ADO	Infrastructure

8.2 Risk Severity Distribution

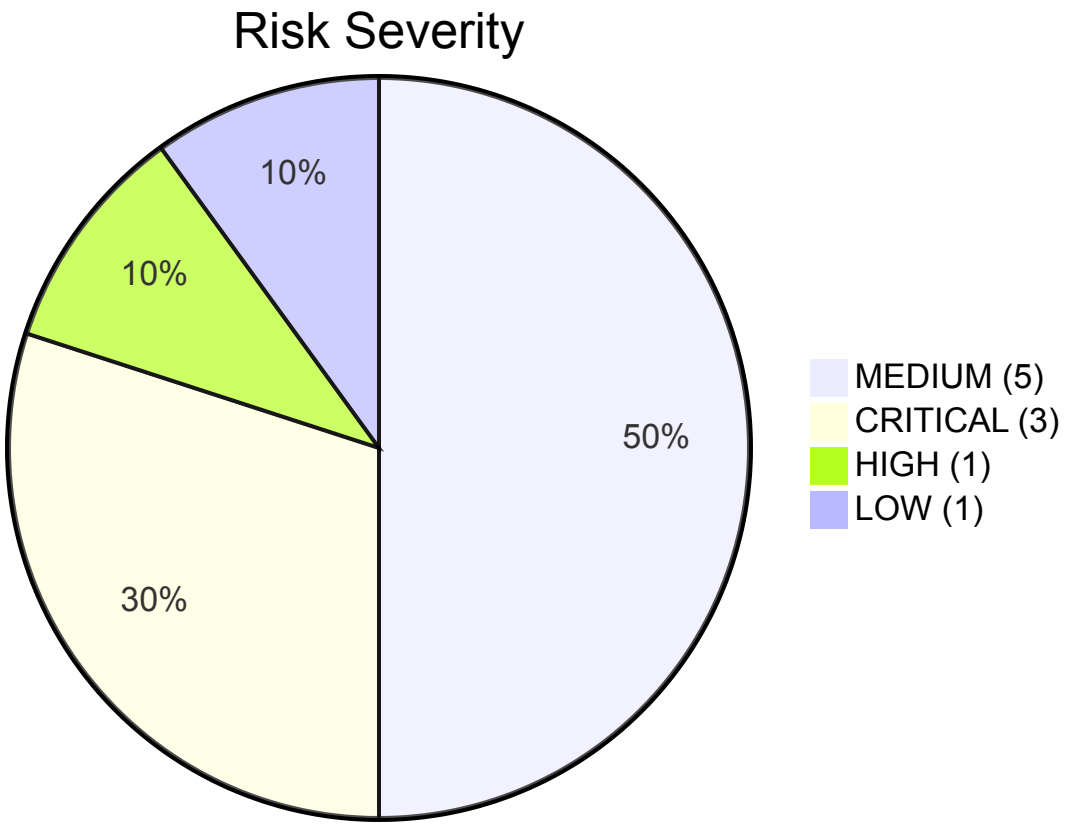

---

9. Prioritized Remediation Actions

P0 — Immediate (This Week)

#	Action	Owner	Rationale
1	**Enable branch protection** on `develop` (FE) and `dev` (BE) requiring at least 1 PR review before merge	Ramon / DevOps	Stops direct pushes and forces code review

#	Action	Owner	Rationale
2	**Mandate PR workflow** — no developer may push directly to integration branches	Karl / Team	Earl's 7 direct pushes on Day 1 bypass all quality gates
3	**Triage defect #200773** (password reset) — move to Active, assign investigation	Earl / Karl	Production-impacting issue should not sit in New
4	**Adopt ADO work item ID convention** — all branches, commits, and PR titles must include `AB#<ID>`	Karl / Team	Zero traceability is an audit-blocking finding

P1 — This Iteration

#	Action	Owner	Rationale
5	**Rebalance Earl's workload** — defer #200184 (Ticket Migration) or assign Roden to support	Karl	26 tasks at 6h/day is burnout/delivery risk
6	**Cliff must activate tasks** — pick 1-2 stories to start immediately	Cliff / Karl	12 tasks in New on Day 2 with zero GitHub activity
7	**Assign spike #200780** to an owner	Karl	Unassigned work creates ambiguity
8	**Create deployment tasks** for Roden under relevant stories	Karl / Roden	Zero-task members create false idle signals

P2 — This PI

#	Action	Owner	Rationale
9	**Add CODEOWNERS** to both repos	Earl / Cliff	Ensures automatic review assignment
10	**Add PR template** (`.github/PULL_REQUEST_TEMPLATE.md`)	Team	Enforces description, WI reference, testing checklist

#	Action	Owner	Rationale
11	**Standardize dev branch naming** — both repos should use `develop` or `dev`, not both	Karl	Reduces confusion
12	**Clean up stale branches** — delete ~40 merged branches	Team	Reduces noise, improves branch list readability
13	**Add CI quality gates** — lint and test on PR creation	DevOps	Currently only deploy workflows exist
14	**Plan QA handoff cadence** — mid-sprint checkpoints instead of end-of-sprint batch	Jerlyn / Karl	Prevents QA crunch in final days

---

10. Iteration Burndown Baseline (Day 2 Snapshot)

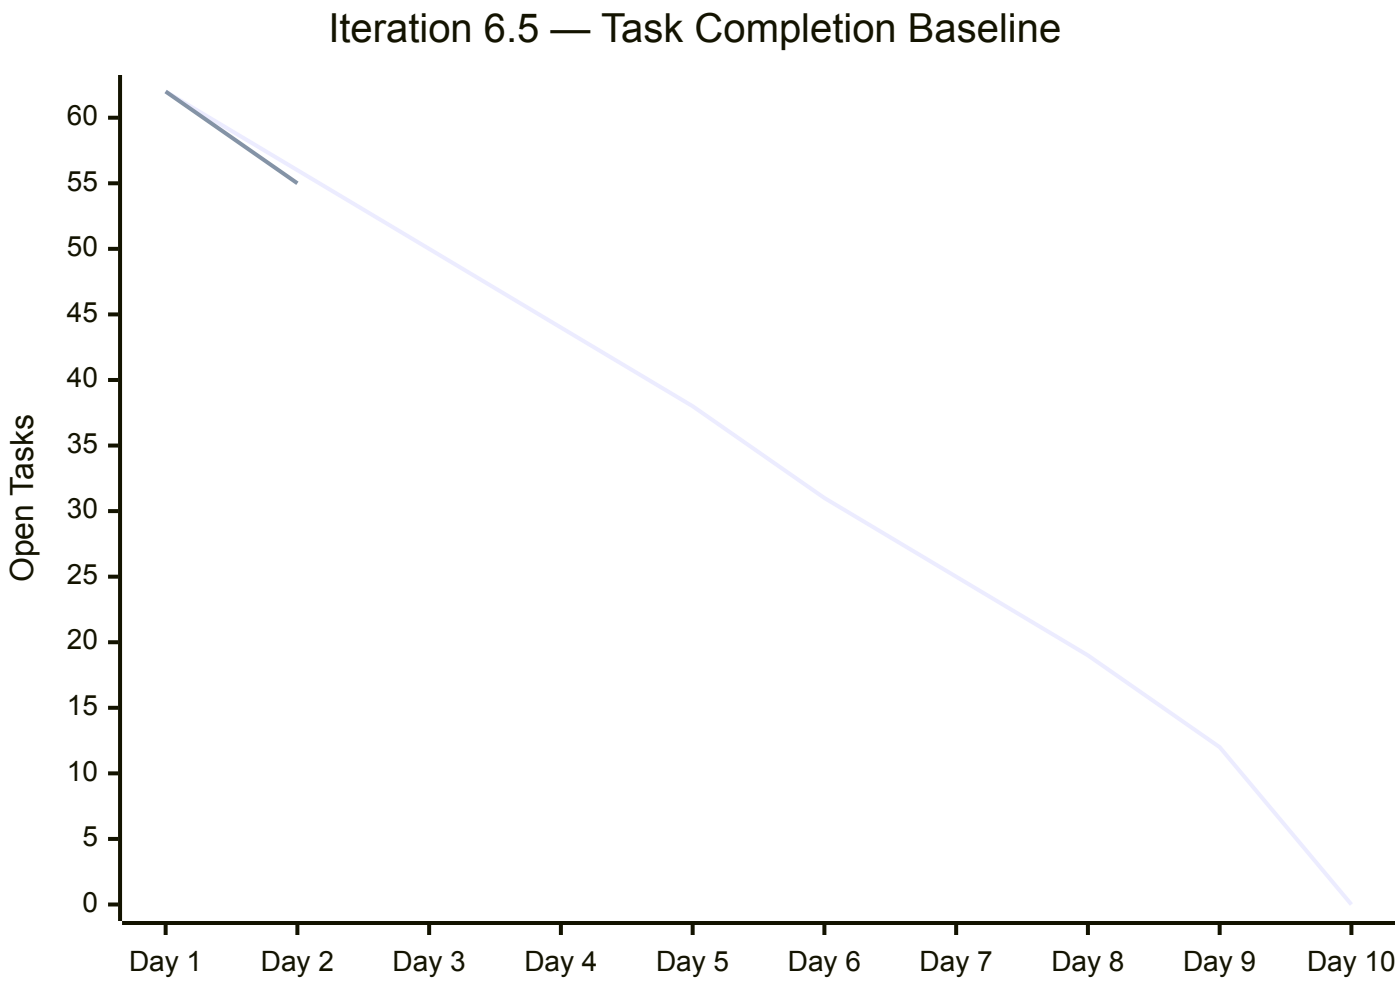

> At Day 2, 4 tasks are closed (55 remaining + 3 active). Ideal burndown rate is ~6.2 tasks/day. Current rate of ~3.5/day is below ideal but within acceptable range for iteration kickoff.

---

11. Remediation Tracker — Carryover from Previous Audits

Tracking recommendations from the March 9 and March 10 audits:

#	Recommendation	Priority	Status	Evidence
1	Branch protection on develop/dev	CRITICAL	❌ Not Started	All branches show `protected: false`
2	Mandate code reviews	CRITICAL	❌ Not Started	0 reviews found (PR #65 self-merged, Earl direct pushes)
3	Add PR template	CRITICAL	❌ Not Started	No `.github/PULL_REQUEST_TEMPLATE.md`
4	Configure CODEOWNERS	CRITICAL	❌ Not Started	No `CODEOWNERS` file in either repo
5	Standardize branch naming	HIGH	❌ Not Started	Mixed conventions: `feature/`, `bug/`, `story/`, `test/`, `enabler/`
6	Standardize dev branch naming	HIGH	❌ Not Started	Frontend: `develop`, Backend: `dev`
7	Clean up stale branches	HIGH	❌ Not Started	41 + 16 = 57 branches
8	Add CI pipeline (lint/test)	HIGH	❌ Not Started	Only deploy workflows exist
9	Adopt conventional commits	MEDIUM	❌ Not Started	`_clean` used as commit message 3× on Day 1
10	Meaningful PR titles & descriptions	MEDIUM	❌ Not Started	PR #65 body is generic
11	ADO work item IDs in GitHub artifacts	**NEW**	❌ Not Started	0 of 10 commits/1 PR reference any WI ID

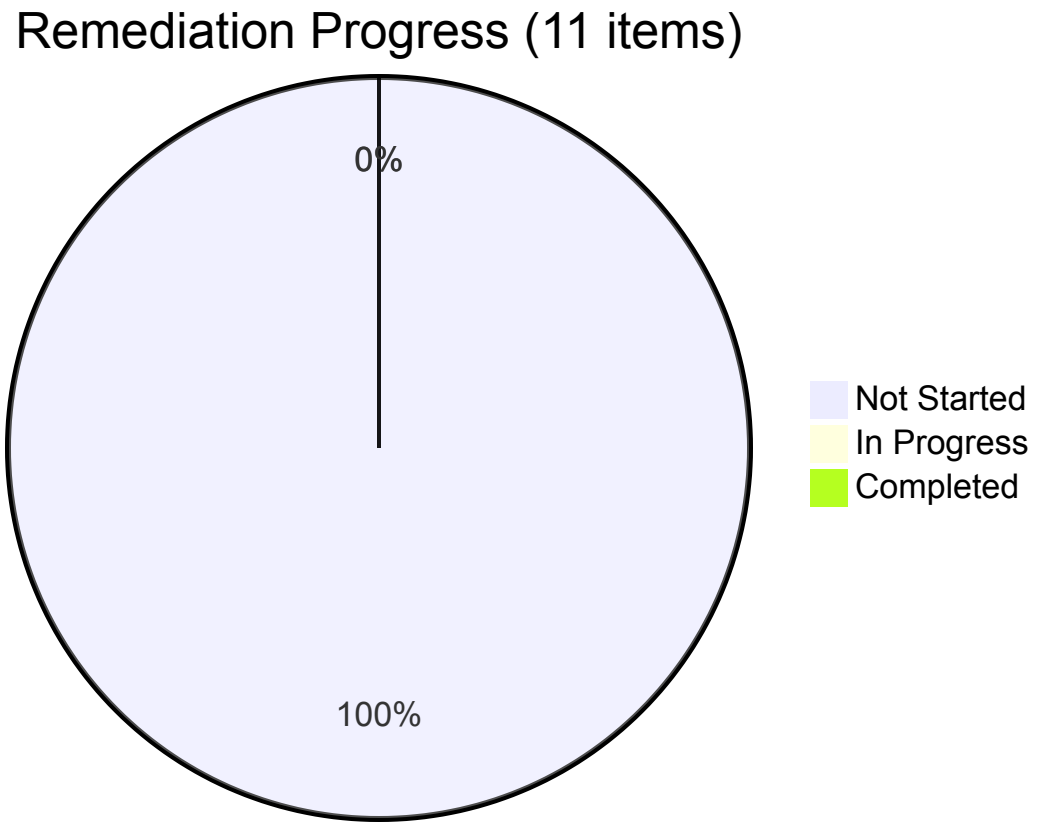

Remediation Score: 0/11 (0%) — No previous audit recommendations have been implemented.

---

12. Audit Metadata

Field	Value
Audit ID	`AUDIT_2026-03-10_202500`
Generated	2026-03-10T20:25:00Z
Updated	2026-03-10 (GitHub data restored)

Field	Value
Iteration	Iteration 6.5 (2026-03-09 to 2026-03-22)
ADO Team	AA Development Team
ADO Board	Stories and Deliverables
GitHub Repos	`jairosoft-com/autoallies-version2` (41 branches), `jairosoft-com/autoallies-api-core` (16 branches)
GitHub Status	✅ Available (credentials restored during audit)
Scope Exclusions	No other boards, teams, projects, or repositories analyzed
Previous Audits	`AUDIT_2026-03-09_000000.md`, `AUDIT_2026-03-10_000000.md`
Data Sources	ADO Iteration API, ADO Work Items API, ADO Capacity API, GitHub REST API (PRs, commits, branches, reviews)

End of audit report.
